

# A414 Edinburgh Way

Latest progress – February 2020

# A414 Edinburgh Way

Latest progress – Feb 2020

**Edinburgh Way – Gates Ford to Harlow Mil Roundabout**

We have completed all of the capping layer through this section.





# A414 Edinburgh Way

Latest progress – Feb 2020

Edinburgh Way – Gates Ford to Harlow Mil Roundabout

We have commenced placing type 1, in preparation for Kerbs to be laid.





# A414 Edinburgh Way

## Latest progress – Feb 2020

### Edinburgh Way – River Way Roundabout – East Road

Here we have completed the excavation for the new road along with the placement of the capping layer.





# A414 Edinburgh Way

## Latest progress – Feb 2020

### Edinburgh Way – River Way Roundabout – East Road

Here we have commenced placement of kerbs.





# A414 Edinburgh Way

## Latest progress – Feb 2020

### Edinburgh Way – East Road Corner

We have exposed a short section of gas pipe that needs moving and are in the process of resolving this with Cadent Gas.






# A414 Edinburgh Way

## Harlow Mill Roundabout Working Area Layout Sketch

Q1 – Q5 are the working areas we refer to for our site works around Harlow Mill Roundabout. These areas are referenced in the following slides.

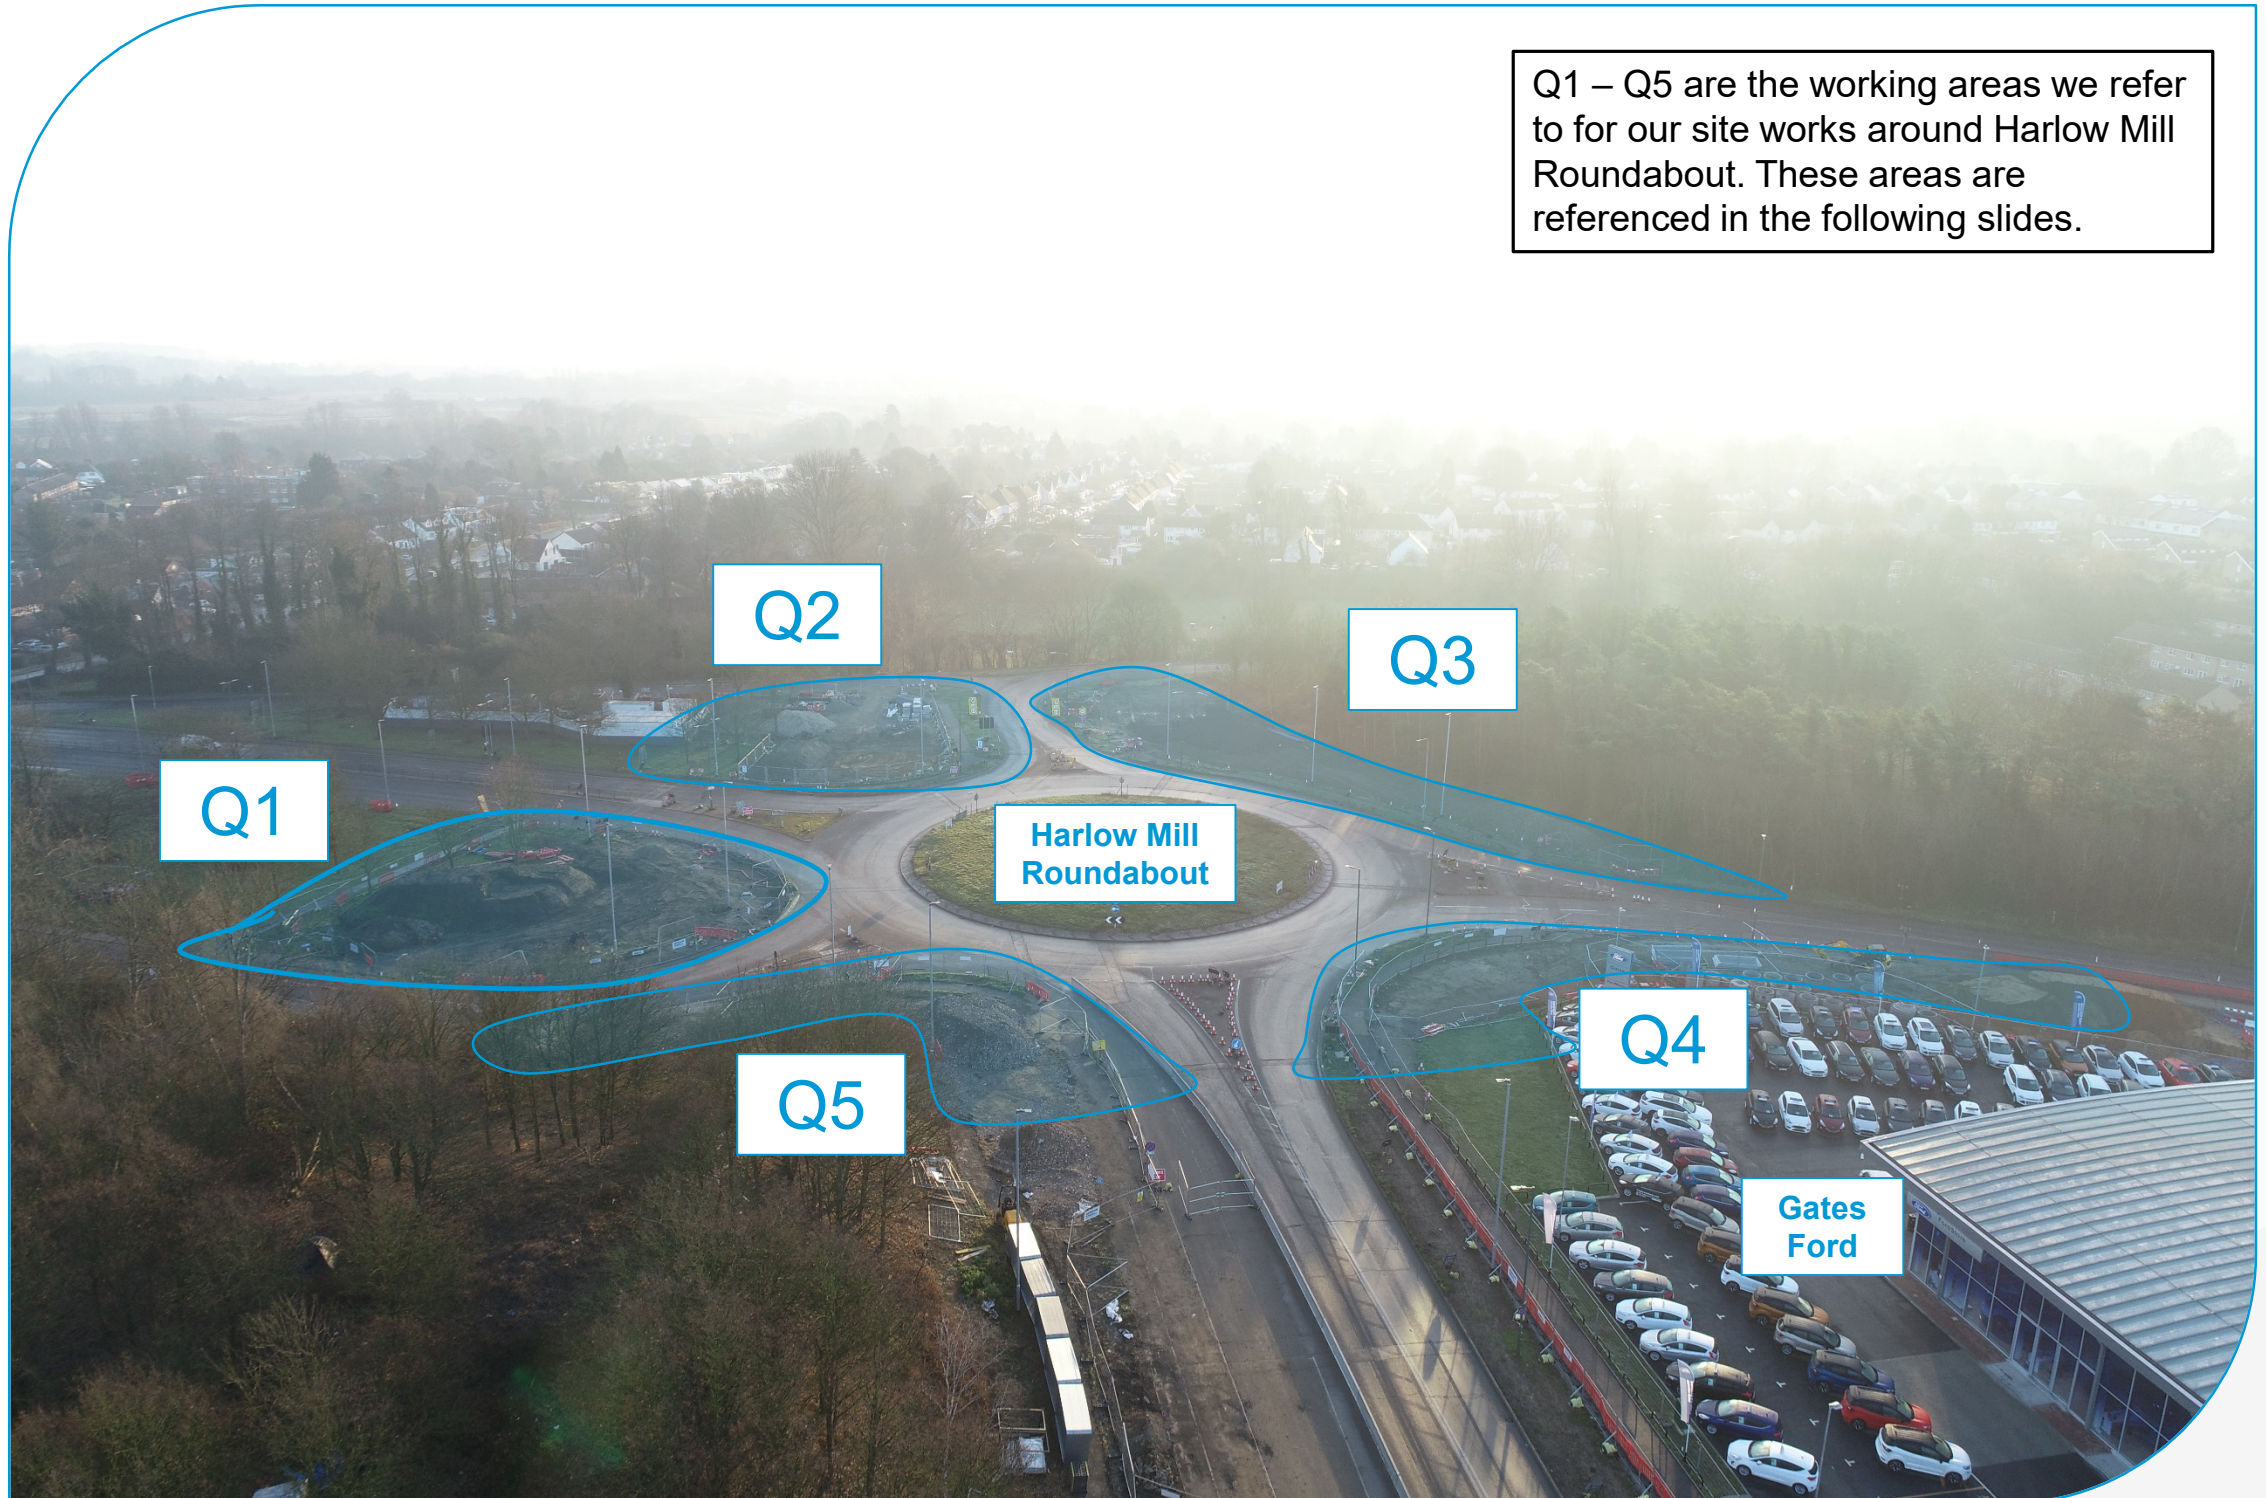



# A414 Edinburgh Way

## Latest progress – Feb 2020

### Edinburgh Way – Roundabout

Roundabout preparations have included concreting the narrow areas, and bringing up the type 1 to finished subbase level.





## A414 Edinburgh Way

### Looking into the future

We have now created an update visualisation and fly through of the scheme. Please scan the QR code below or use the link to look into the future.



[https://www.youtube.com/  
watch?v=oOSjYzuwPr4](https://www.youtube.com/watch?v=oOSjYzuwPr4)



# A414 Edinburgh Way

## Edinburgh Way – North side

### Planned activities March 2020

#### Phase

North side phase 1

North side phase 2

North side phase 3

#### Main Works

- Start installing signs
- Start installing signs
- Start installing signs
- Commence installation of Pedestrian Guard Rail



# A414 Edinburgh Way

## Edinburgh Way – South side

### Planned activities March 2020

#### Phase

#### Main Works

##### South side phase 1

- Complete type 1 in preparation for surfacing
- Complete reconstruction of the exit from the St James Centre.

##### South side phase 2

- Complete type 1 in preparation for surfacing
- Complete tie ins to East Road
- Complete construction of the entrance to the Athena estate.

##### South side phase 3

- Complete type 1 in preparation for surfacing
- Complete construction of the entrance into Templefields.


##### South side phase 4

- Complete type 1 in preparation for surfacing
- Commence drainage to Q2 & Q3 of Harlow Mill Roundabout.



# A414 Edinburgh Way

## Phase Sections

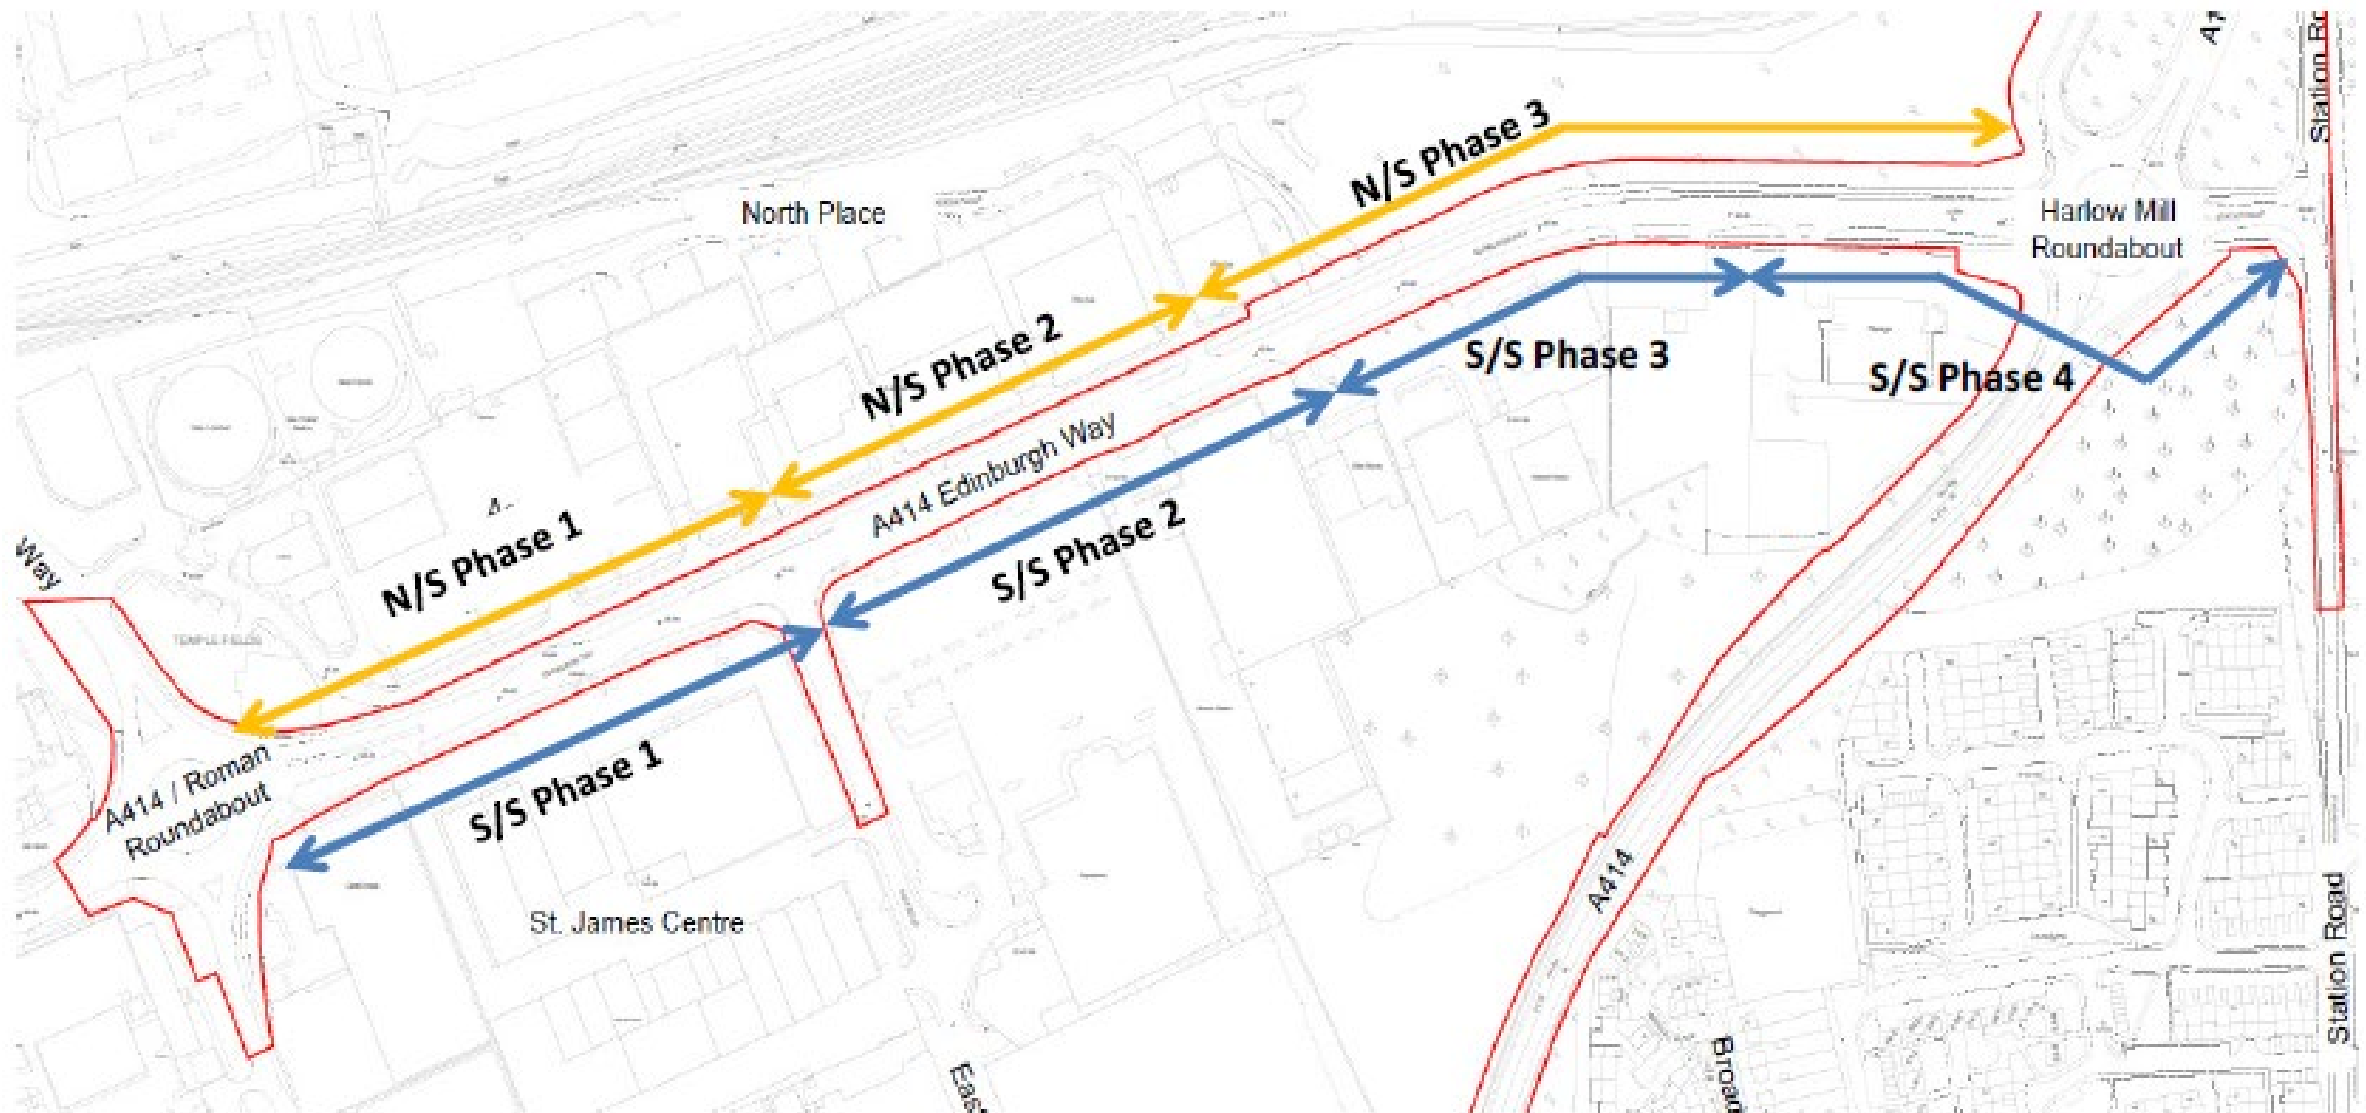



## A414 Edinburgh Way

### No Right Turn Signs



There are a series of No Right Turn signs in place along the scheme. These are in place for the safety of the public, the workforce and are also a legal requirement. Please ensure they are adhered to.
