

# A414 Edinburgh Way

## Latest progress – Nov 2019

### Edinburgh Way – The Big Traffic Switch

Some of you may have noticed that we have switched the traffic management over recently so that we can construct the southern half of the scheme. Therefore those of you that drive the scheme regularly are now driving on the new future east bound alignment. It also means the scheme drainage is circa 90% complete and the overall scheme circa 65% complete. We have also opened the new North side footpath removing all of the heras fence panels that had been in place for a few years!! Don't forget to visit our visualisation of the scheme to see how it will look in the completed state.



# A414 Edinburgh Way

## Latest progress – Nov 2019

### Edinburgh Way – Drainage & Road box Construction

With the traffic switch complete we have now commenced excavation to the southern side of the scheme. We have started at the western end of the scheme and completed the first manhole, road box excavation and placing of founding material to date. We have also encountered some services that have impacted progress. These are now resolved allowing the scheme to build momentum again.



First Manhole installed on the southern side of the scheme opposite Peugeot.


Area of new road widening

# A414 Edinburgh Way

## Latest progress – Nov 2019

### Edinburgh Way – Drainage East Road / Edinburgh Way Junction

Those of you that use East Road regularly will have noticed that the junction off Edinburgh Way has had traffic management in place for the past few weeks. This had been to allow us to construct the new surface water drainage catch pits in that cross the junction. We have also installed 6 gully pots and one 225mm drain pipe run so that the area drains correctly in the future. The light grey concrete section in the photo below shows the new drainage recently installed.

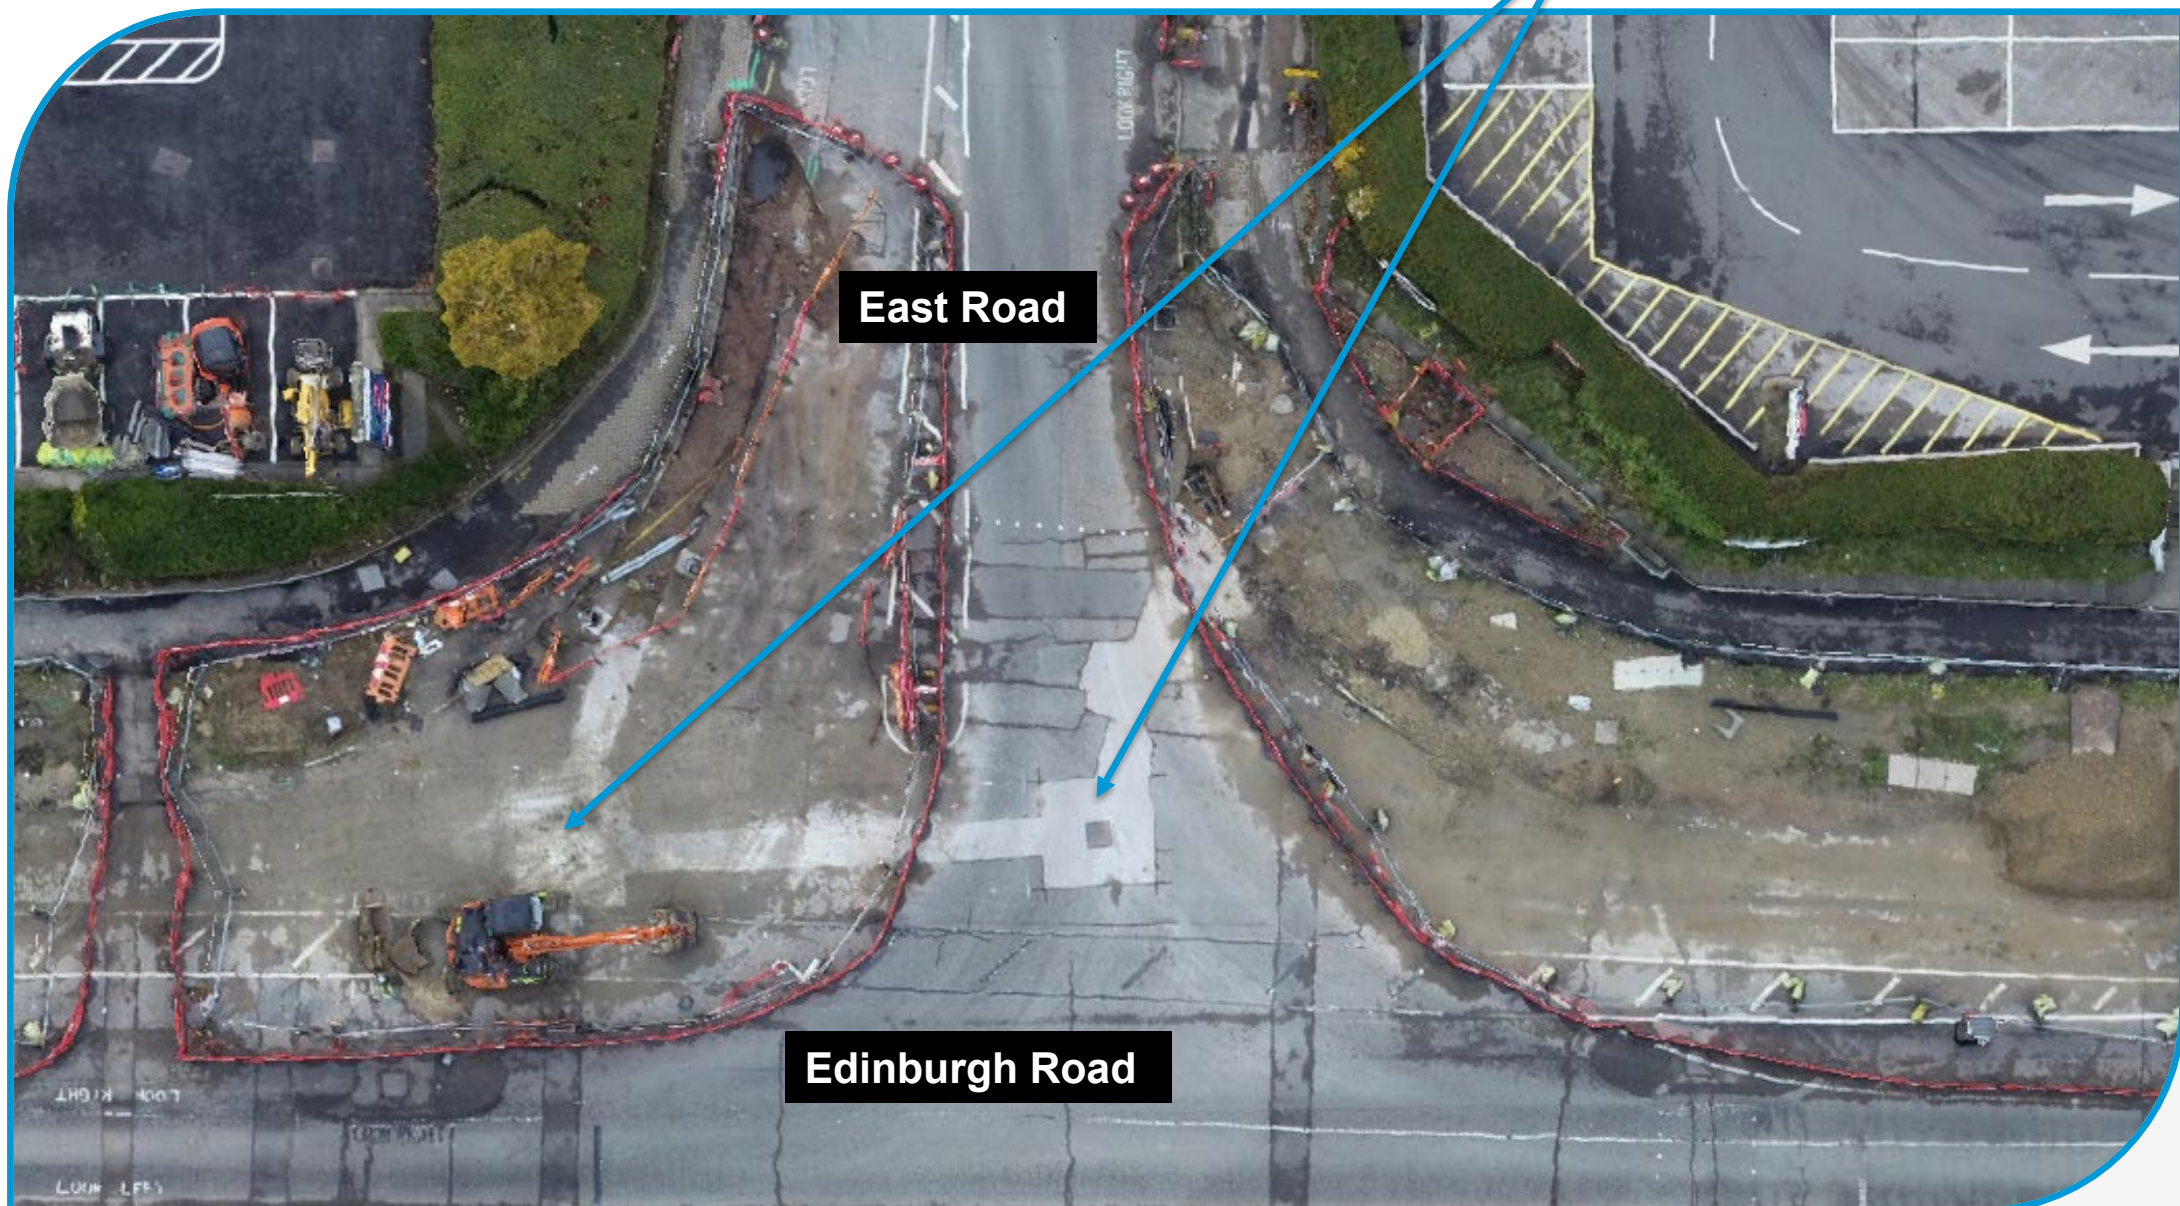

# A414 Edinburgh Way

## Harlow Mill Roundabout Working Area Layout Sketch

Q1 – Q5 are the working areas we refer to for our site works around Harlow Mill Roundabout. These areas are referenced in the following slides.



# A414 Edinburgh Way

Latest progress – Nov 2019

## Harlow Mill Roundabout Construction

We have recently started the re construction of Harlow Mill Roundabout. In the finished state the roundabout will be smaller than it currently is allowing for more capacity to hold vehicles. We have to date installed five catch pits, 80 meters of drainage pipe, completed the excavation and placing of the founding material.

The brown earth in the photo is the original roundabout size.

The light grey around the edge is the new road widening.

The light grey small circles are the catch pits that have been installed for the drainage system.



# A414 Edinburgh Way

## Where to find out more

Further details about the scheme can be found on the Essex County Council website at:

- <https://www.essexhighways.org/highway-schemes-and-developments/major-schemes/a414-edinburgh-way-cambridge-road.aspx>
- Alternatively click on the QR code provided.
- Information about other works in the area can be found at: [www.roadworks.org](http://www.roadworks.org) or via the QR code on the right.



For general enquiries, please contact the Essex County Council customer service team:

- By telephone 0345 603 7631
- Online: <http://essex.gov.uk/enquiries>
- Or use the QR code provided



# A414 Edinburgh Way

## Looking into the future

We have now created a full visualisation of how the finished scheme will look. Please scan the QR code below or use the link to look into the future.



<https://youtu.be/8dUmeeqYn1g>

# A414 Edinburgh Way

## Edinburgh Way – South side

### Planned activities December 2019

#### Phase

North side phase 1

North side phase 2

North side phase 3

#### Main Works

- Start installing signs
- Start installing signs
- Start installing signs



# A414 Edinburgh Way

## Edinburgh Way – South side

### Planned activities December 2019

#### Phase

#### Utility Diversions

#### Main Works

#### South side phase 1

- Complete

- Continue with box cut
- Install 2 Catch pits

#### South side phase 2

- Complete

- Install catch pit
- Commence box cut

#### South side phase 3

- Complete


- Install catch pit

#### South side phase 4

- Complete

- Install catch pits by Gates Ford.
- Complete kerbs to Harlow Mill Roundabout .
- Place base course surfacing to Harlow Mill Roundabout

# A414 Edinburgh Way Phase Sections

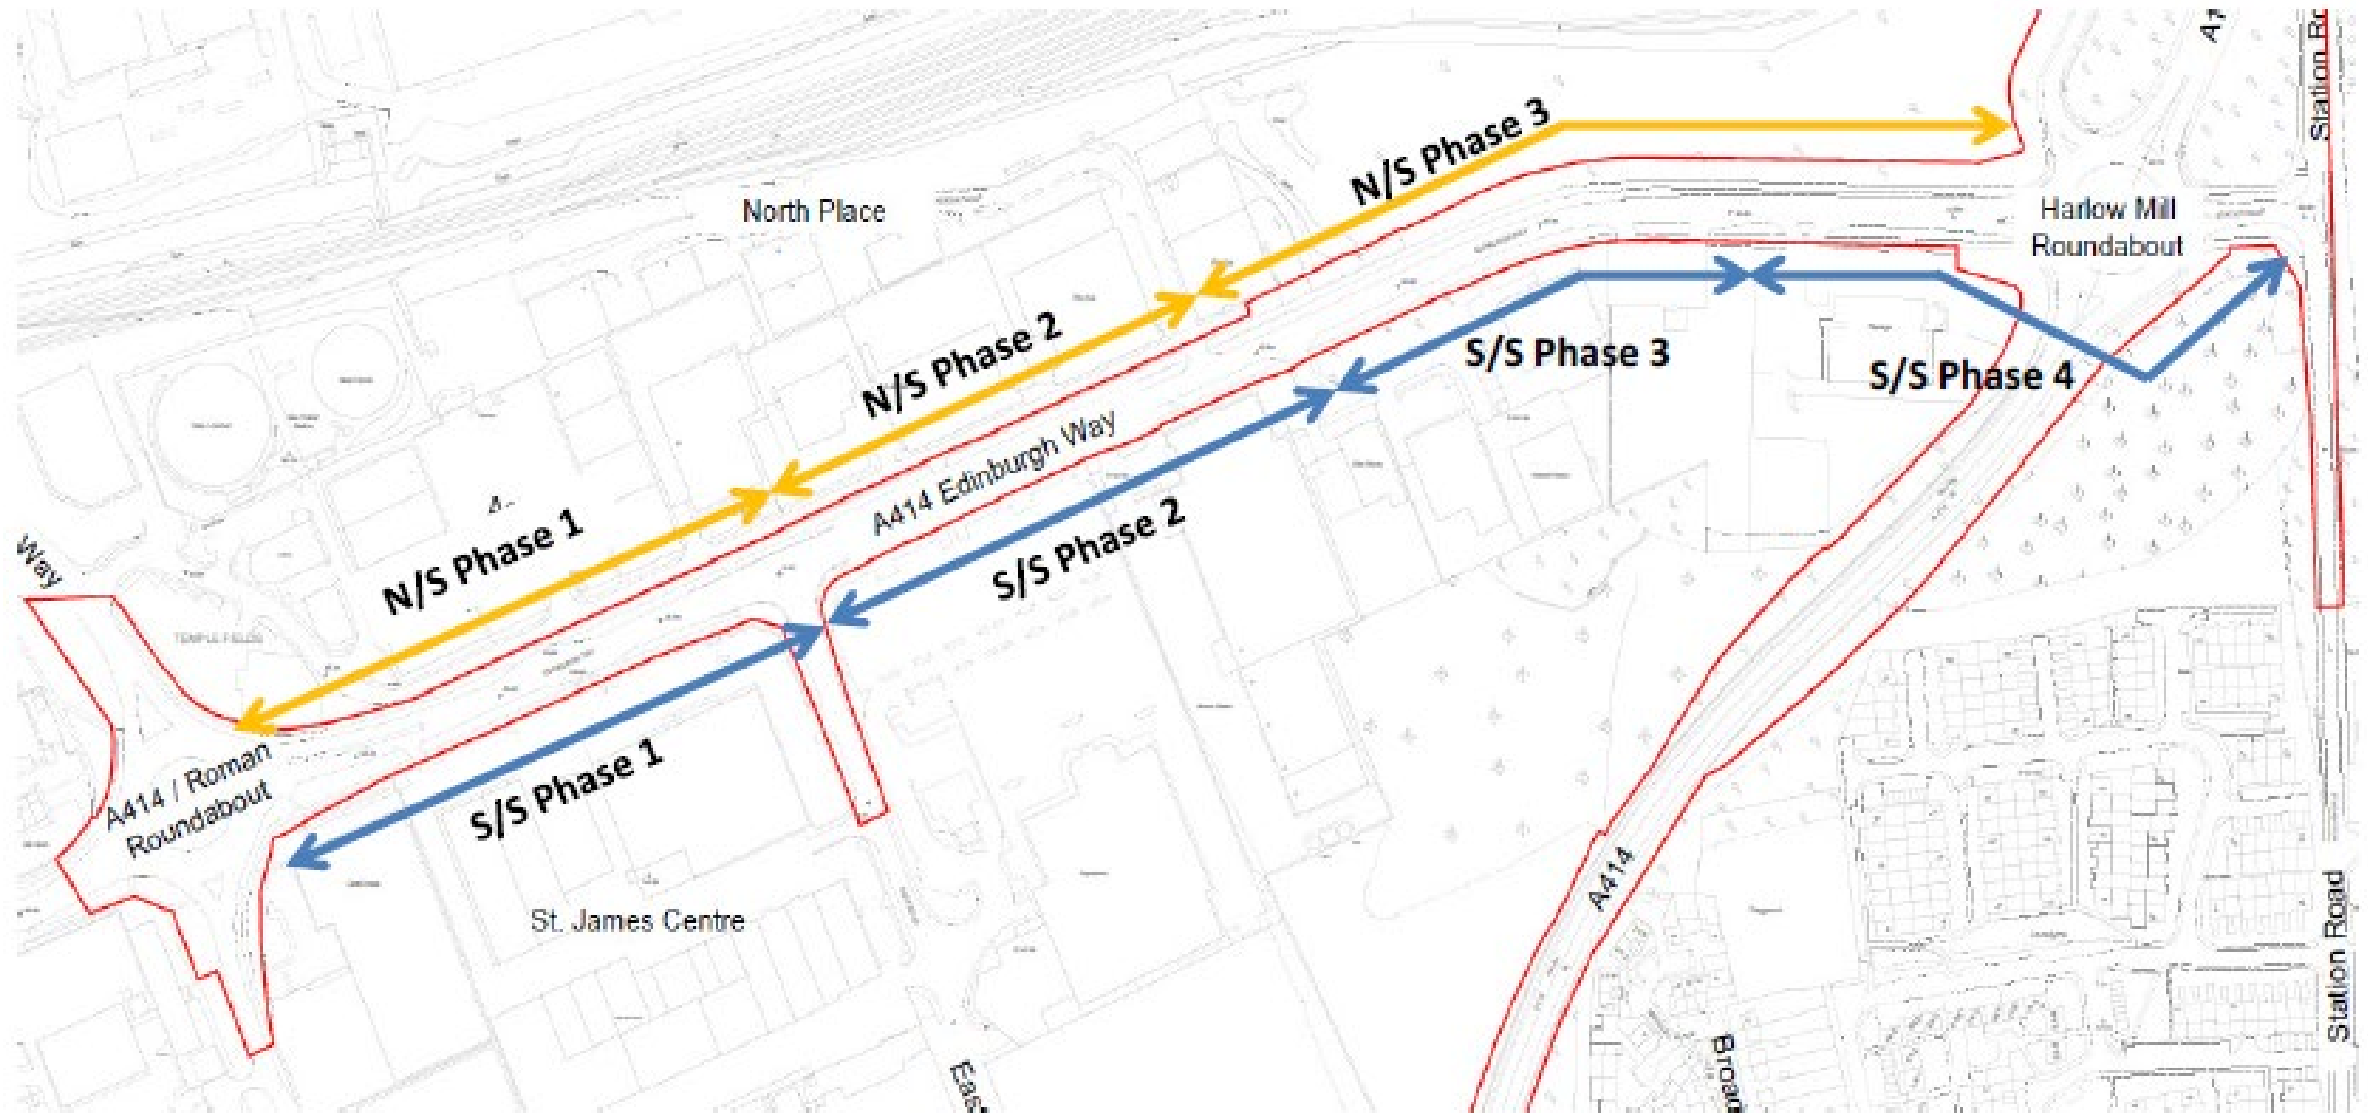

## A414 Edinburgh Way

### No Right Turn Signs



There are a series of No Right Turn signs in place along the scheme. These are in place for the safety of the public, the workforce and are also a legal requirement. Please ensure they are adhered to.
