

# A414 Edinburgh Way

## Latest progress – October 2018

### Works progress to support future carriageway widening on north and south of Edinburgh Way:

- We have commence construction of the crib retaining wall that will provide the support to the widen A414 south as you approach Harlow Mill Roundabout from the M11. This has involved:
  - The removal of 2500m<sup>3</sup> of the existing embankment,
  - The installation of a concrete foundation
  - The installation of a recycled plastic (Ecocrib) wall filled with 500t of 40mm-75mm stone.
- Temporary footpath construction is on going to the Southside of Edinburgh way. This will give a safe route for pedestrians whilst the new drainage system is installed on the north side of the carriageway.
- Whilst the roundabout construction is underway there will be changes to the local footpaths. Signed diversions will be in place, please keep an eye out for these.

# A414 Edinburgh Way

## Latest progress – October 2018

**Works progress to support future carriageway widening on north and south of Edinburgh Way:**

- Completed all drainage repairs that were required across the scheme.
- We had a successful week of nights at the beginning of October that included:
  - The installation all of the street lamp columns and heads along Edinburgh Way
  - Installation of the final duct crossing across North Place
  - The installation of the final BT ducts along East Road
  - All these works were completed on time with no incidents

**Thank you for your patience while Edinburgh Way was closed**

**Please keep an eye on these boards for further notices and updates**

# A414 Edinburgh Way

## Latest progress – October 2018

### Photos of the works

The Crib Retaining Wall along the A414:



# A414 Edinburgh Way

## Edinburgh Way – North side

### Planned activities November - December 2018

<b>Phase</b>	<b>Utility Diversions</b>	<b>Main Works</b>
<b>North side phase 1</b>	<ul style="list-style-type: none"><li>◆ BT Openreach diversion</li><li>◆ Trench to be backfilled</li></ul>	<ul style="list-style-type: none"><li>◆ New drainage</li></ul>
<b>North side phase 2</b>	<ul style="list-style-type: none"><li>◆ BT Openreach diversion</li><li>◆ Trench to be backfilled</li></ul>	<ul style="list-style-type: none"><li>◆ New drainage</li></ul>
<b>North side phase 3</b>	<ul style="list-style-type: none"><li>◆ Trench to be backfilled</li></ul>	<ul style="list-style-type: none"><li>◆ New drainage</li></ul>


# A414 Edinburgh Way

## Edinburgh Way – South side

### Planned activities November - December 2018

<b>Phase</b>	<b>Utility Diversions</b>	<b>Main Works</b>
<b>South side phase 1</b>	<ul style="list-style-type: none"><li>↗ Connections and testing</li></ul>	<ul style="list-style-type: none"><li>↗ Footpath kerbs and asphalt</li></ul>
<b>South side phase 2</b>	<ul style="list-style-type: none"><li>↗ Connections and testing</li></ul>	<ul style="list-style-type: none"><li>↗ Footpath kerbs and asphalt</li></ul>
<b>South side phase 3</b>	<ul style="list-style-type: none"><li>↗ Connections and testing</li></ul>	<ul style="list-style-type: none"><li>↗ Footpath kerbs and asphalt</li><li>↗ Commence drainage installation to Harlow Mill Roundabout</li></ul>
<b>South side phase 4</b>	<ul style="list-style-type: none"><li>↗ Connections and testing</li></ul>	<ul style="list-style-type: none"><li>↗ Complete retaining wall on the A414 South</li><li>↗ Commence drainage along the A414 South</li></ul>

# A414 Edinburgh Way Phase Sections

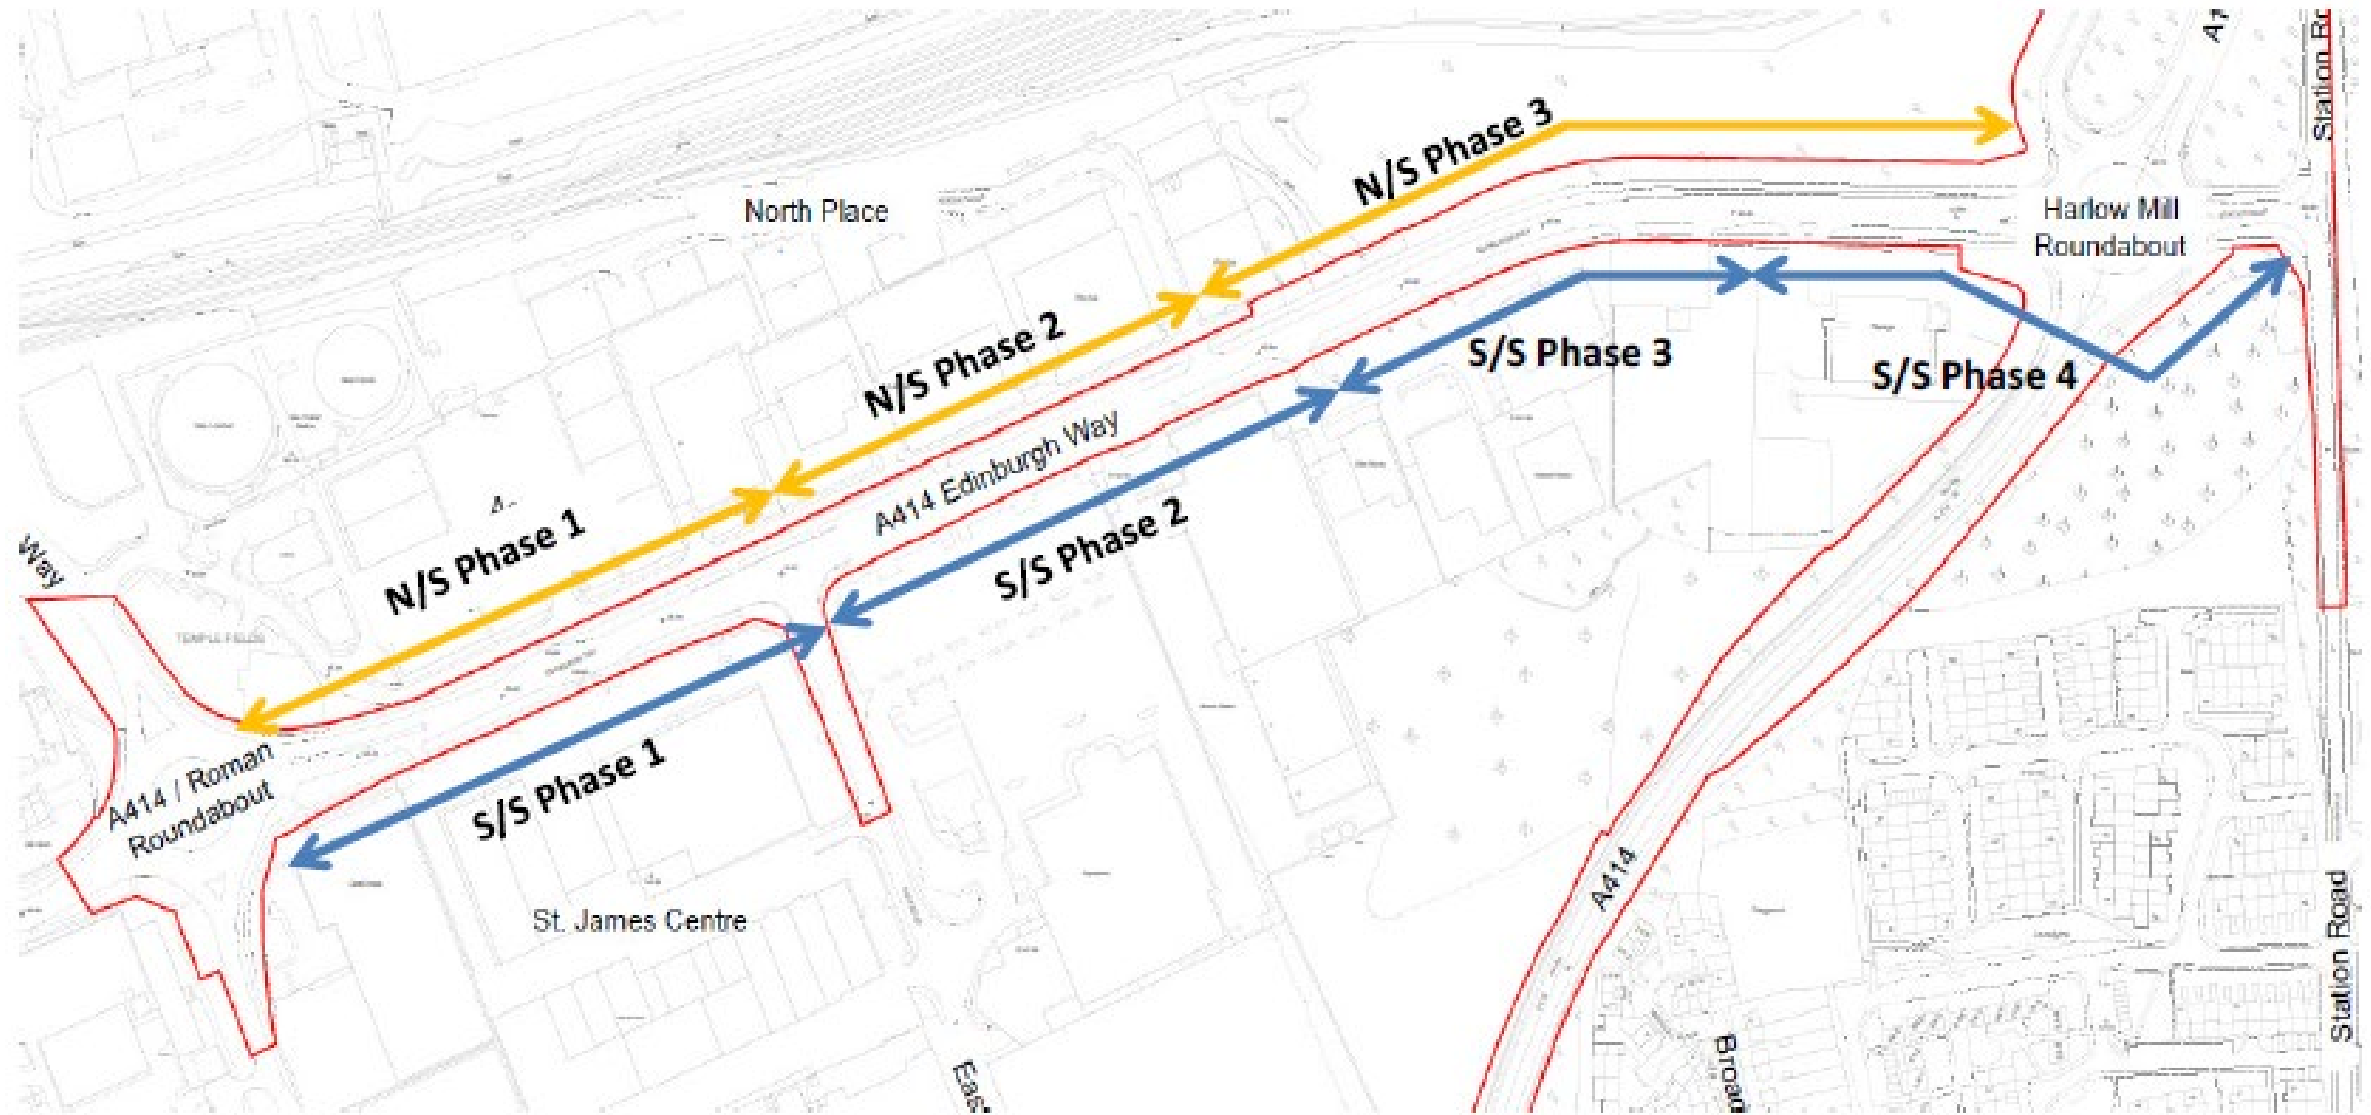

## A414 Edinburgh Way

### No Right Turn Signs



There are a series of No Right Turn signs in place along the scheme. These are in place for the safety of the public, the workforce and are also a legal requirement. Please ensure they are adhered to.
