

Edinburgh Way – Road box Construction – Harlow Mill Roundabout – North Place

We have now placed the first layer of surfacing to this area. This will allow us to move the traffic to the north side of Edinburgh Way providing space for the southern side to be constructed. In the future we will place the final surfacing course to the road. We have also completed all of the footpath construction through this area ready for footpath surfacing to be completed. We have installed the traffic signal ducts for the future traffic lights and raised all of the existing service covers to the finished footpath level.













Edinburgh Way - Road box Construction - North Place - River Way Roundabout

We have now completed all of the road box excavation through this section along with the placement of the road foundation and kerbs. We have completed 80% of the footpath construction through this area along with the traffic signal ducts and the raising of the service covers and lids to the finished levels.











INFRASTRUCTURE

MORGAN

SINDALL

Edinburgh Way – Drainage

We have completed the final section of drainage to the north side of the scheme








A414 Edinburgh Way

Harlow Mill Roundabout Working Area Layout Sketch



Q1 – Q5 are the working areas we refer to for our site works around Harlow Mill Roundabout. These areas are referenced in the following slides.

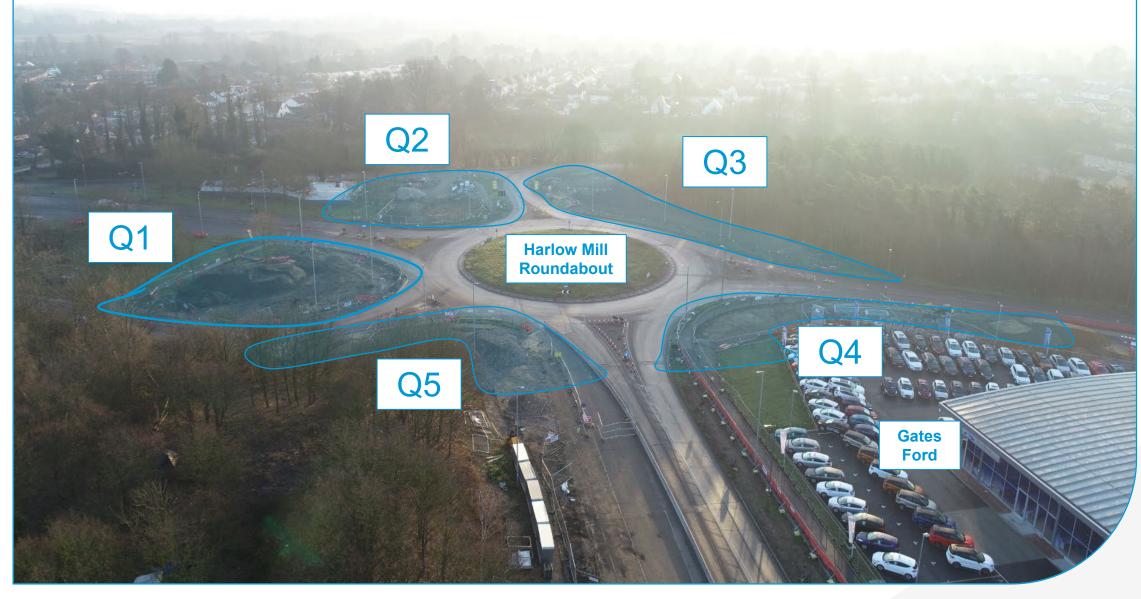








A414 Southern Leg (Q4) – Road Box Construction

The surfacing has been carried out. The batter has been shaped and topsoil placed on it. The footpath edging kerbs have been laid.

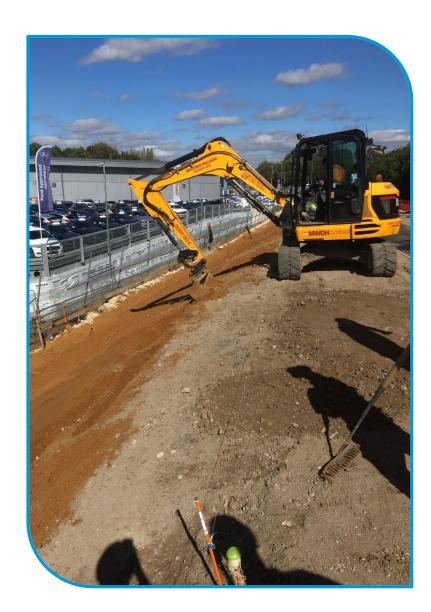









A414 Edinburgh Way Where to find out more



Further details about the scheme can be found on the Essex County Council website at:

- https://www.essexhighways.org/highway-schemes-and-developments/major-schemes/a414-edinburgh-way-cambridge-road.aspx
- Alternatively click on the QR code provided.
- Information about other works in the area can be found at: www.roadworks.org or via the QR code on the right.

For general enquiries, please contact the Essex County Council customer service team:

- By telephone 0345 603 7631
- Online: http://essex.gov.uk/enquiries
- Or use the QR code provided





A414 Edinburgh Way Looking into the future



We have now created a full visualisation of how the finished scheme will look. Please scan the QR code below or use the link to look into the future.



https://youtu.be/8dUmeeqYn1g





A414 Edinburgh Way Edinburgh Way – North side



Planned activities October 2019

Phase

North side phase 1

North side phase 2

North side phase 3

Main Works

- Complete drainage. Complete road box excavation, placing of founding material, place kerbs and first layer of surfacing.
- Complete kerbs and place surfacing.
 Complete footpath excavation and place edging kerbs.
- Complete the first layer of asphalt. Complete footpath excavation and place edging kerbs.





A414 Edinburgh Way

Edinburgh Way – South side

Planned activities October 2019




Phase	Utility Diversions	Main Works
South side phase 1	Openreach cable pulling and connectionsVodafone cable installation	 Remove remaining old street light columns
South side phase 2	Openreach cable box installationVodafone cable installation	 Remove remaining old street light columns
South side phase 3	Openreach cable box installationVodafone cable installation	 Remove remaining old street light columns
South side phase 4	 Vodafone Ducts 	 Remove remaining old street light columns. Complete box cut and installation of the founding material.



A414 Edinburgh Way Phase Sections



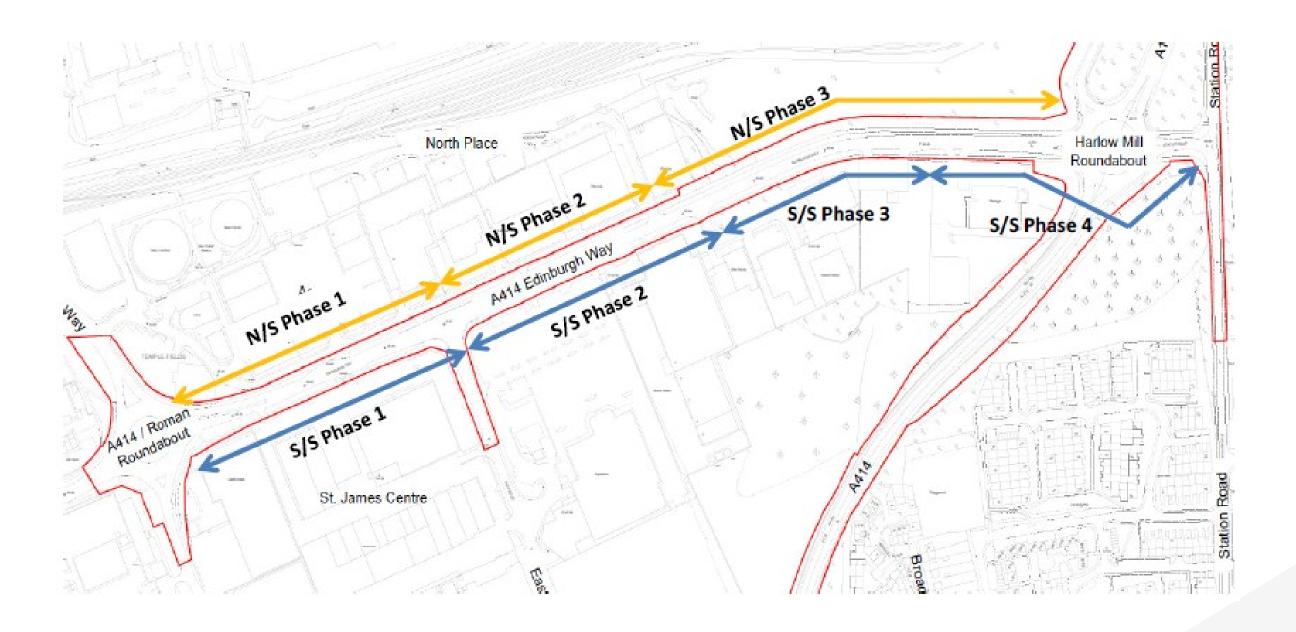





A414 Edinburgh Way

No Right Turn Signs





There are a series of No Right Turn signs in place along the scheme. These are in place for the safety of the public, the workforce and are also a legal requirement. Please ensure they are adhered to.



