

M11 Jct 8 Improvement Scheme – Project Update May 2023




Birchanger Lane Phase 1 Completed

Phase 1 of Birchanger Lane has now been completed. This includes the installation of new drainage and footpaths along Birchanger Lane. There have been some unexpected delays due to additional services and obstructions being found under the ground but these have now been resolved. The remainder of the works on Birchanger Lane will continue in phase 2.

Birchanger Lane Phase 2 In Progress

Phase 2 of Birchanger Lane involves the construction of the new section of road that will connect Birchanger Lane to the new junction. This is shown in the diagram below.

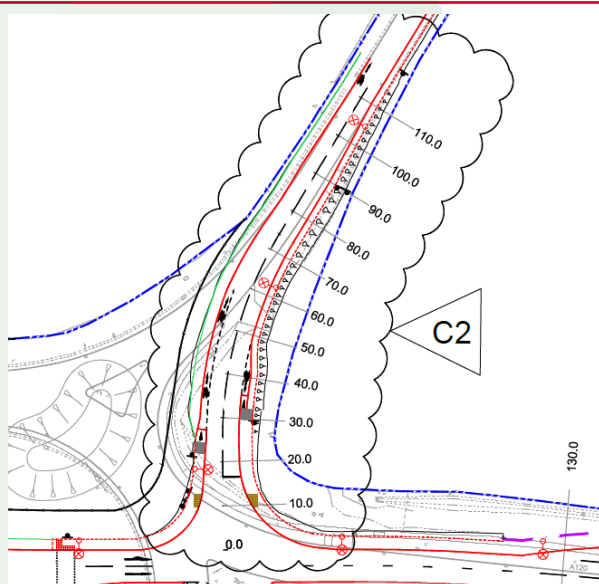

Scan left, or [click here](#) for education and work experience opportunities

M11 Jct 8 Improvement Scheme – Project Update May 2023

A120 Progress

The standard capping beams on the A120 have now been completed with only the 2 sloped capping beams remaining.

The working platform has now been removed which has allowed the road formation to commence.

The completion of this first phase of the road construction will allow the lights on the A120 to be removed at the end of May.

The first phase of drainage and construction of the sign base below ground has also been completed on the east section of the A120 which will allow the next phase of piling to commence on the week commencing 9th May 2023.

M11 Jct 8 Offslips

The traffic management has now been placed on the 2 offslips of the M11 Junction 8. This will allow the works to commence to construct the additional lanes on both offslips.

There will be further weekend works undertaken on the 12th May 2023 to allow the completion of diversion works. This will require the closure of the northbound offslip. These works are being undertaken in conjunction with other works planned by National Highways to minimise the disruption to the public.



Scan right, or [click here](#) for community support opportunities

M11 Jct 8 Improvement Scheme – Project Update May 2023


Upcoming Traffic Management:

The temporary traffic lights will be removed from the A120 on 31st May 2023. This will allow the traffic to run straight through the new junction. This will result in there being no right turn out of Dunmow Road to access the M11 Jct 8. The new arrangement is shown in the diagram below.



**A120/Stansted Road
at which to turn
around to access
the M11.**

**Birchanger Lane
A120 Roundabout**

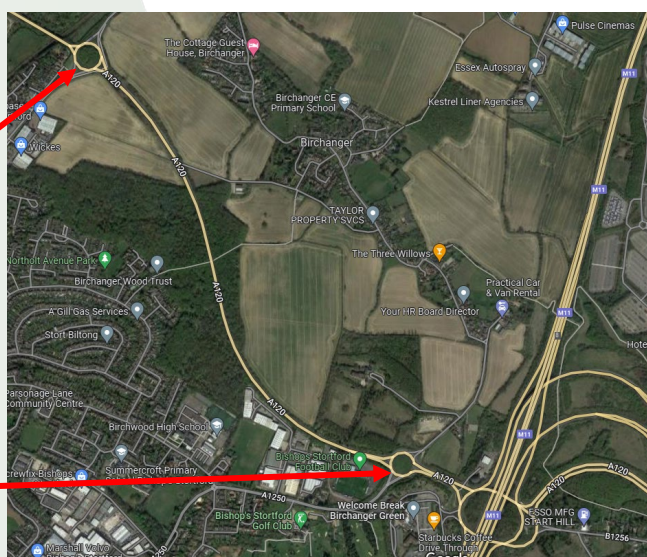

Contact us: 07442981580

M11Jct8Enquiries@4projectsmail.com
